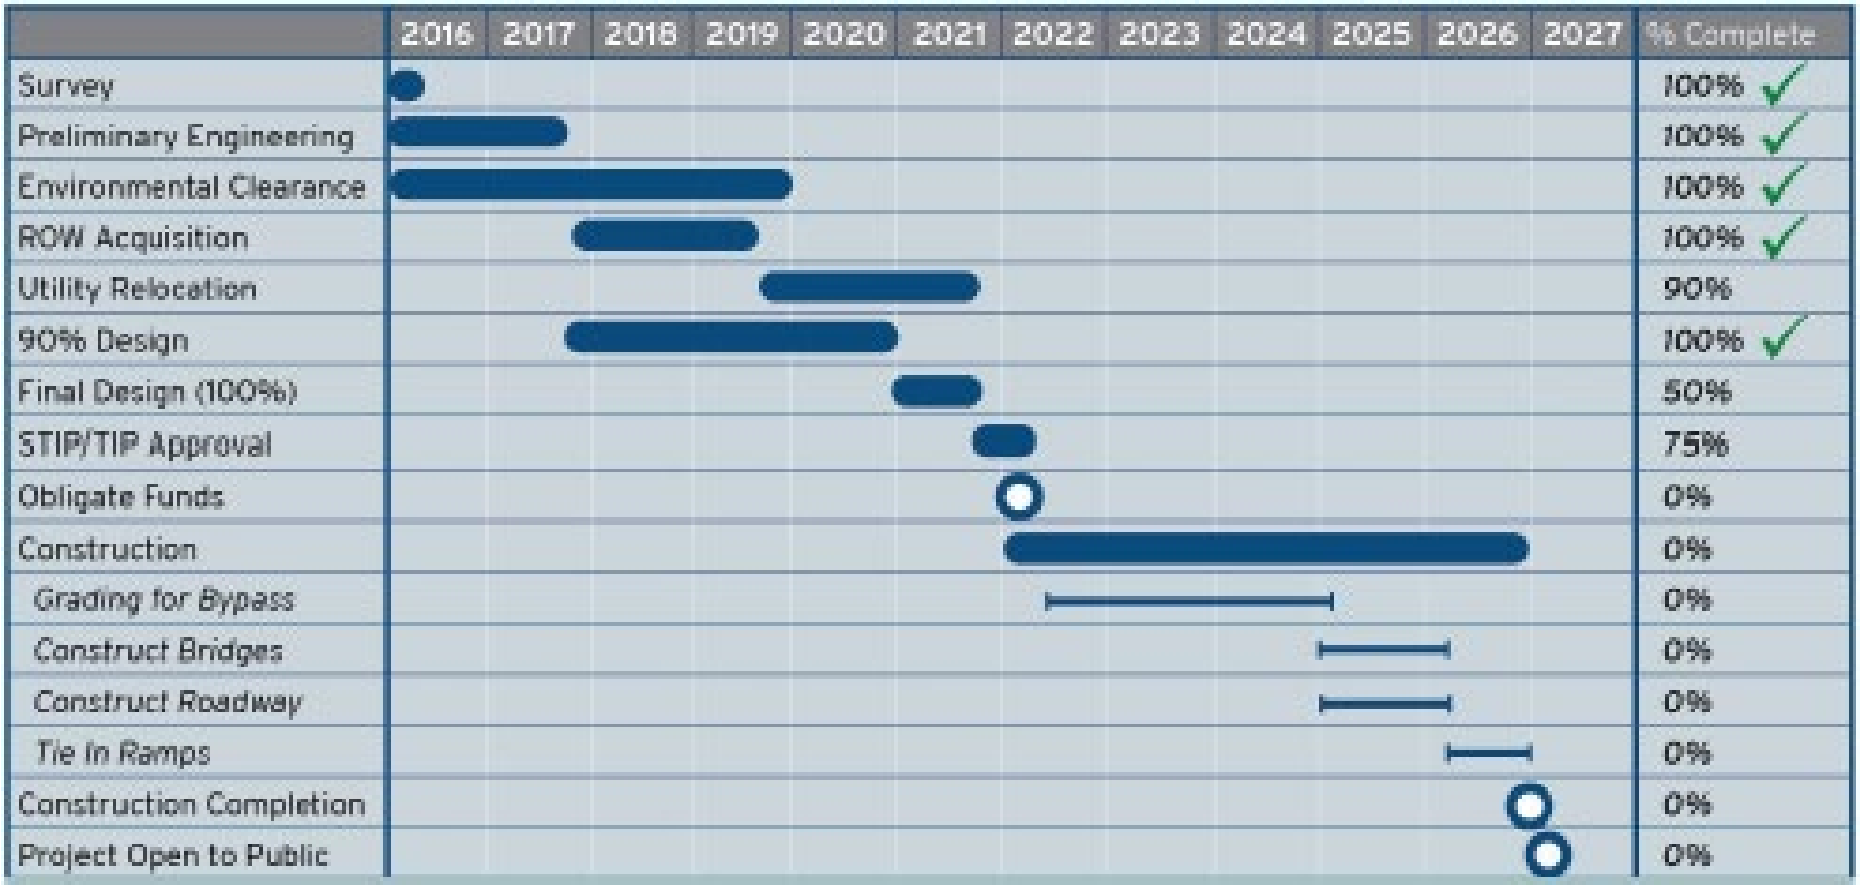
2016
2017
2018
2019
2020
2021
2022
2023
2024
2025
2026
2027
% Complete
Survey
100%
Preliminary Engineering
100%
Environmental Clearance
100%
ROW Acquisition
100%
Utility Relocation
90%
90% Design
100%
Final Design (100%)
50%
STIP/TIP Approval
75%
Obligate Funds
0%
Construction
0%
Grading for Bypass
0%
Construct Bridges
0%
Construct Roadway
0%
Tie In Ramps
0%
Construction Completion
0%
Project Open to Public
0%
